

ATHLETIC FIELDS MASTER PLANNING

Staff Report: Sept 2016 Update

Recreation Department

Mayor's Office of Strategic Planning and Community Development


SomerStat

September 27, 2016

Somerville, MA

Background

- City staff undertook an Athletic Fields Master Planning effort in late 2015 and early 2016, which included two community meetings and a presentation to the Board of Aldermen.
- This presentation is a second update to the plan. It is an abbreviated version of previous presentations, which are available online:
 - June 2016 update:
 http://www.somervillema.gov/sites/default/files/documents/2016%20Fields%20Master%20Planning%20Staff%20Report%20Update_June.pdf
 - March 2016:
 http://www.somervillema.gov/sites/default/files/documents/20
 16%20athletic%20fields v2 DRAFT.pdf
- September 2016 updates are in orange
- June 2016 updates are in purple

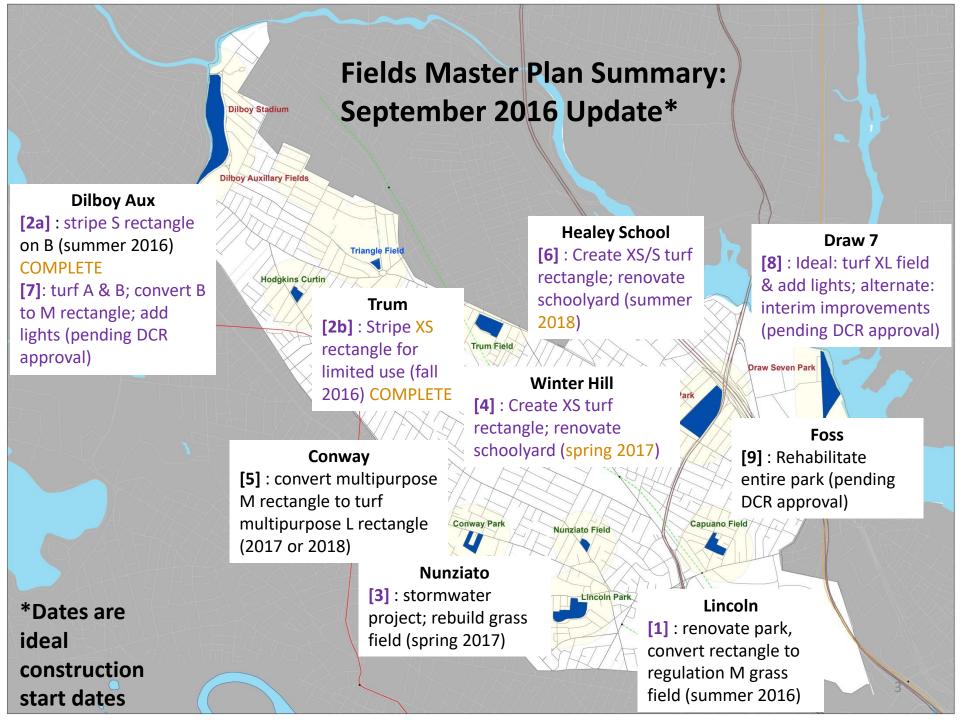

Step 1: Lincoln Park renovation

- 1. Description: rehabilitate entire park, including massive stormwater storage project
 - a. Convert non-regulation L rectangle to M rectangle
 - New drainage, irrigation & lighting for rectangle & diamond fields
- 2. Recommended surface: grass
- 3. Ideal timeline:
 - a. Construction summer 2016 through fall 2017
 - a. Schoolyard & underground stormwater storage system complete
 - b. Field rest through summer 2018
 - c. Field online fall 2018
- 4. Displaced uses: SHS girls soccer, SHS ultimate frisbee, SYSL, SHS softball, SYSBL
 - a. All displaced uses relocated
- 5. Requires cooperation from non-City party: no

Step 2a: Dilboy Aux B interim improvements

- 1. Description: stripe S rectangle over field
 - a. Provides swing space for Lincoln construction
- 2. Recommended surface: n/a
- 3. Ideal timeline: summer 2016
 - a. Completed August 2016
- 4. Displaced uses: essentially none due current underutilization of Dilboy B
- 5. Requires cooperation from non-City party: no

Step 2b: Limited rectangle use at Trum

- 1. Description: stripe XS rectangle at Trum
 - a. Provides swing space for displaced play from Lincoln
- 2. Recommended surface: n/a
- 3. Ideal timeline: fall 2016
 - a. Completed August 2016
- 4. Displaced uses: none
- 5. Requires cooperation from non-City party: no

Step 3: Nunziato renovation

- 1. Description: rehabilitate entire park, including massive stormwater storage project
 - Rebuild S grass rectangle with new drainage, irrigation, and lighting
- 2. Recommended surface: grass
- 3. Ideal timeline:
 - a. Design summer 2016 through winter 2017
 - i. Design services contract being executed
 - ii. Kickoff meeting Tuesday, 9/27
 - b. Construction late spring/summer 2017 though spring 2019
 - c. Field rest fall 2019 through spring 2020
 - d. Field online fall 2020
- 4. Displaced uses: SHS ultimate frisbee, SYSL U8
- 5. Requires cooperation from non-City party: no



Step 4: Winter Hill XS field

- 1. Description: construct XS rectangle on lowest level of Winter Hill schoolyard
 - a. Provides swing space for Nunziato construction
 - b. Provides opportunity to rehabilitate Winter Hill schoolyard
- 2. Recommended surface: turf
- Ideal timeline:
 - a. Field design summer 2016
 - i. Survey complete
 - ii. Design services contract being executed
 - iii. Kickoff meeting soon
 - b. Field construction spring 2017
 - c. Field online summer 2017
 - d. Schoolyard project fall 2016 through end of 2017
 - i. City applying for CPA funds for schoolyard construction
- 4. Displaced uses: none
- 5. Requires cooperation from non-City party: no

Step 5: Conway renovation

- Description: convert M multipurpose field to L multipurpose field, including new drainage, irrigation, and lighting
 - a. Maintain 2 S diamonds
 - Repair retaining wall
 - c. Remediate potential soil contamination
 - d. Add storm water storage
- Recommended surface: turf
- 3. Ideal timeline:
 - a. Begin construction 2017 or 2018
 - City pursuing survey & geotech analysis (pending BOA funding approval)
- 4. Displaced uses: SHS football, SYSL
- 5. Requires cooperation from non-City party: no

Step 6: Healey School XS/S field

- 1. Description: construct XS or S rectangle at Healey School
 - a. Provides additional capacity
 - b. Provides opportunity to rehabilitate Healey schoolyard
- Recommended surface: turf
- Ideal timeline:
 - a. Design summer 2017 through spring 2018
 - a. CPA-funded Healey to Mystic planning study completed summer 2016
 - b. City applying for CPA funds for schoolyard design
 - c. City pursuing survey & geotech analysis (pending BOA funding approval)
 - b. Construction summer 2018 through summer 2019
 - c. Field online fall 2019
- 4. Displaced uses: none
- 5. Requires cooperation from non-City party: no

Step 7: Dilboy Aux renovation

- Description: rehabilitate Dilboy Aux A & B with new irrigation, drainage, and lighting
 - a. Permanently convert underutilized S diamond to M rectangle
- 2. Recommended surface: turf
- 3. Ideal timeline: fall 2019
- 4. Displaced uses: SHS soccer, SYSL
- 5. Requires cooperation from non-City party: yes

On hold pending conversations with DCR

Step 8: Draw 7 renovation

- Description: renovate entire park, including creation of XL rectangle field with new irrigation, drainage, and lighting
- 2. Recommended surface: turf
- 3. Ideal timeline: spring 2020 through fall 2020
- 4. Displaced uses: none
- 5. Requires cooperation from non-City party: yes

On hold pending conversations with DCR

Step 9: Foss renovation

- 1. Description: Rehabilitate entire park with new playing fields, irrigation, drainage, and lighting
- 2. Recommended surface: To be determined
- 3. Ideal timeline: To be determined
- 4. Displaced uses: To be determined
- 5. Requires cooperation from non-City party: yes

Field Maintenance Updates

- BOA approved Administrative Order to include fields maintenance under a new Parks & Recreation department
- BOA approved Fields Division budget in the FY17 Budget
 - Director of Operations interviews scheduled
- City issued a RFP for Maintenance Plan consultant August 2016; responses due week of 9/26
 - Assessment of current conditions due December 2016
 - Maintenance plan due April 2017
 - Staff training spring 2017

Key next steps

- Flexible RFQ issued for design services for up to 4 projects (Winter Hill, Nunziato, Conway, Healey). Complete
- 2. BOA request for design funds for Winter Hill & Nunziato. Complete → kickoff meetings soon
- 3. Incorporate projects into FY17-FY26 CIP. Ongoing
- 4. Issue RFP for fields maintenance plan. Complete
- 5. Continue conversations with DCR re: Draw 7, Dilboy & Foss. Ongoing
- 6. Pursue surveys and geotech analyses at Conway and Healey, pending BOA funding approval

